



Task Name	Duration	Start	Finish	Predecessors	Resource
<b>PEKERJAAN PERSIAPAN</b>	<b>165 days</b>	<b>Fri 06/07/18</b>	<b>Mon 17/12/18</b>		
Papan nama proyek	7 days	Fri 06/07/18	Thu 12/07/18		
Pagar sementara dari seng gelombang tin	0 days	Fri 06/07/18	Fri 06/07/18		
Pengukuran dan Pemasangan bouwplank	14 days	Fri 13/07/18	Thu 26/07/18	2	
Pembersihan lahan awal dan akhir proyek	25 days	Fri 13/07/18	Mon 06/08/18	2	
Air dan listrik kerja	158 days	Fri 13/07/18	Mon 17/12/18	2	
Rambu-rambu proyek	14 days	Fri 06/07/18	Thu 19/07/18	2SS	
Uji material	158 days	Fri 13/07/18	Mon 17/12/18	7FS-7 days	
<b>PEKERJAAN STRUKTUR</b>	<b>105 days</b>	<b>Fri 06/07/18</b>	<b>Thu 18/10/18</b>		
<b>PEKERJAAN GALIAN DAN URUGAN</b>	<b>42 days</b>	<b>Fri 20/07/18</b>	<b>Thu 30/08/18</b>		
<b>Elevasi. - 1.150</b>	<b>14 days</b>	<b>Fri 20/07/18</b>	<b>Thu 02/08/18</b>		
Galian pilecape P2 sampai dengi	14 days	Fri 20/07/18	Thu 02/08/18	4FS-7 days	
<b>Elevasi. - 0.700</b>	<b>35 days</b>	<b>Fri 20/07/18</b>	<b>Thu 23/08/18</b>		
Galian pilecape P1 sampai dengi	35 days	Fri 20/07/18	Thu 23/08/18	12SS	
Galian pilecape P2 sampai dengan 1r	35 days	Fri 20/07/18	Thu 23/08/18	12SS	
Urugan pasir bawah pilecape P1 tebi	21 days	Fri 03/08/18	Thu 23/08/18	14SS+14 days	
Urugan pasir bawah pilecape P2 tebi	21 days	Fri 03/08/18	Thu 23/08/18	15SS+14 days	
Urugan tanah kembali bekas galian pi	14 days	Fri 17/08/18	Thu 30/08/18	16FS-7 days;17F	
<b>PEKERJAAN BETON</b>	<b>105 days</b>	<b>Fri 06/07/18</b>	<b>Thu 18/10/18</b>		
<b>LANTAI 1</b>	<b>70 days</b>	<b>Fri 20/07/18</b>	<b>Thu 27/09/18</b>		
Cor rabat bawah pilecape tebal	21 days	Fri 24/08/18	Thu 13/09/18	16;17	
Cor rabat bawah lantai tebal = 1	14 days	Fri 14/09/18	Thu 27/09/18	21	
Pondasi tiang pancang square 2	35 days	Fri 20/07/18	Thu 23/08/18	12SS;14SS	
Test pembebanan PDA dan PIT	7 days	Fri 10/08/18	Thu 16/08/18	23FS-14 days	
Bobokan/ cutting kepala tiang pa	28 days	Fri 27/07/18	Thu 23/08/18	23SS+7 days	
Cor pilecape P1 uk. 1600x1600	28 days	Fri 03/08/18	Thu 30/08/18	25SS+7 days	
Cor pilecape P2 uk. (Sesuai Det	28 days	Fri 03/08/18	Thu 30/08/18	25SS+7 days	
Cor kolom K1 400 x 500 mm f'c -	28 days	Fri 24/08/18	Thu 20/09/18	26FS-7 days;27F	
Cor kolom K2 400 x 400 mm f'c -	28 days	Fri 24/08/18	Thu 20/09/18	28SS	




29	Cor kolom K2 400 x 400 mm f'c =	28 days	Fri 24/08/18	Thu 20/09/18	28SS	
30	Cor kolom K2 400 x 400 mm f'c =	28 days	Fri 24/08/18	Thu 20/09/18	28SS	
31	Cor kolom K3 150 x 500 x 500 m	28 days	Fri 24/08/18	Thu 20/09/18	28SS	
32	Cor balok sloof S1 300 x 450 m	28 days	Fri 31/08/18	Thu 27/09/18	28SS+7 days	
33	Cor balok sloof S1 300 x 450 m	28 days	Fri 31/08/18	Thu 27/09/18	29SS+7 days	
34	Cor balok sloof S2 250 x 350 m	28 days	Fri 31/08/18	Thu 27/09/18	29SS+7 days	
35	Cor balok sloof S1 300 x 450 m	28 days	Fri 31/08/18	Thu 27/09/18	32SS	
36	Cor balok sloof S2 250 x 350 m	28 days	Fri 31/08/18	Thu 27/09/18	33SS	
37	Cor balok sloof S3 150 x 450 m	28 days	Fri 31/08/18	Thu 27/09/18	31SS+7 days	
38	Cor balok BT 200 x 450 mm f'c =	28 days	Fri 31/08/18	Thu 27/09/18	32SS	
39	Cor tangga tebal plat bordes : 1f	21 days	Fri 07/09/18	Thu 27/09/18	38SS+7 days	
40	<b>LANTAI 2</b>	<b>35 days</b>	<b>Fri 24/08/18</b>	<b>Thu 27/09/18</b>		
41	Cor kolom K1 400 x 500 mm f'c =	7 days	Fri 14/09/18	Thu 20/09/18	28FF	
42	Cor kolom K2 400 x 400 mm f'c =	7 days	Fri 21/09/18	Thu 27/09/18	41	
43	Cor kolom K3 150 x 500 x 500 m	7 days	Fri 21/09/18	Thu 27/09/18	41	
44	Cor balok B1 400 x 600 f'c = 25	14 days	Fri 24/08/18	Thu 06/09/18	26FS-7 days	
45	Cor balok B1a 400 x 600 f'c = 2	14 days	Fri 24/08/18	Thu 06/09/18	44SS	
46	Cor balok B2 400 x 600 f'c = 25	14 days	Fri 24/08/18	Thu 06/09/18	44SS	
47	Cor balok B3 250 x 400 f'c = 25	14 days	Fri 24/08/18	Thu 06/09/18	44SS	
48	Cor balok B4 200 x 400 f'c = 25	14 days	Fri 24/08/18	Thu 06/09/18	44SS	
49	Cor balok B4a 200 x 400 f'c = 2	14 days	Fri 24/08/18	Thu 06/09/18	44SS	
50	Cor balok B4b 200 x 400 f'c = 2	14 days	Fri 24/08/18	Thu 06/09/18	44SS	
51	Cor balok B5 150 x 500 f'c = 25	14 days	Fri 24/08/18	Thu 06/09/18	44SS	
52	Cor balok B6 400 x 600 f'c = 25	14 days	Fri 24/08/18	Thu 06/09/18	44SS	
53	Cor balok B7 250 x 400 f'c = 25	14 days	Fri 24/08/18	Thu 06/09/18	44SS	
54	Cor balok L1 120 x 750 f'c = 25	14 days	Fri 24/08/18	Thu 06/09/18	44SS	
55	Cor plat lantai A1 t: 140 mm f'c =	14 days	Fri 07/09/18	Thu 20/09/18	54	

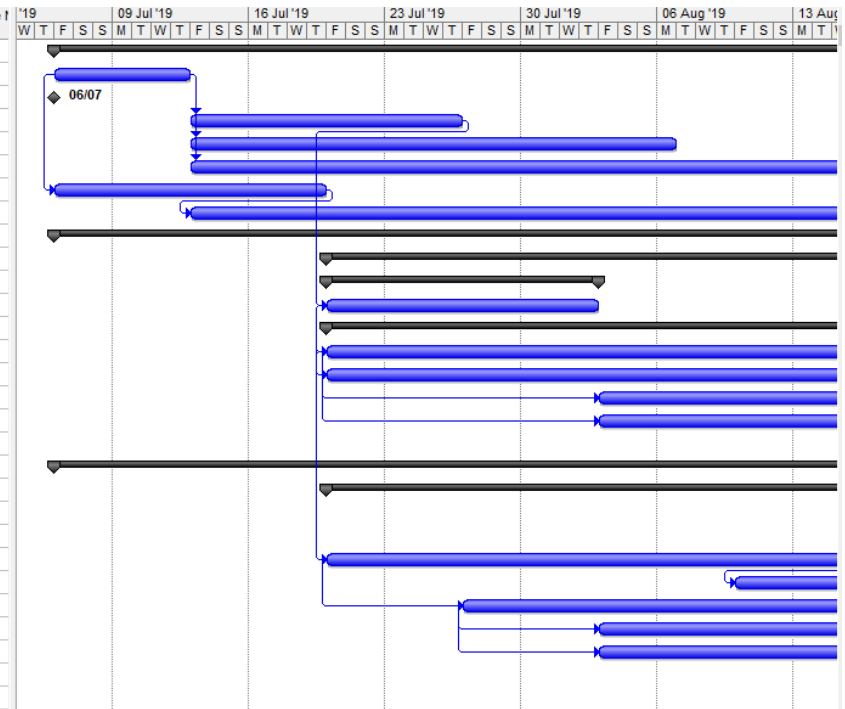


55	Cor plat lantai A1 t. 140 mm f <sub>c</sub> =	14 days	Fri 07/09/18	Thu 20/09/18	54
56	<b>LANTAI ATAP</b>	<b>105 days</b>	<b>Fri 06/07/18</b>	<b>Thu 18/10/18</b>	
57	Cor kolom K1 400 x 500 mm f <sub>c</sub> =	14 days	Fri 21/09/18	Thu 04/10/18	41
58	Cor kolom K2 400 x 400 mm f <sub>c</sub> =	0 days	Fri 06/07/18	Fri 06/07/18	
59	Cor kolom K4 250 x 250 mm f <sub>c</sub> =	14 days	Fri 21/09/18	Thu 04/10/18	57SS
60	Cor balok B1 400 x 600 f <sub>c</sub> = 25	28 days	Fri 14/09/18	Thu 11/10/18	55FS-7 days
61	Cor balok B3 250 x 400 f <sub>c</sub> = 25	28 days	Fri 21/09/18	Thu 18/10/18	60SS+7 days
62	Cor balok B4 200 x 400 f <sub>c</sub> = 25	21 days	Fri 21/09/18	Thu 11/10/18	61SS
63	Cor balok B4c 200 x 400 f <sub>c</sub> = 2	21 days	Fri 21/09/18	Thu 11/10/18	61SS
64	Cor balok B4d 200 x 400 f <sub>c</sub> = 2	21 days	Fri 21/09/18	Thu 11/10/18	61SS
65	Cor balok B5 150 x 500 f <sub>c</sub> = 25	21 days	Fri 21/09/18	Thu 11/10/18	61SS
66	Cor balok B4 200 x 400 f <sub>c</sub> = 25	14 days	Fri 05/10/18	Thu 18/10/18	65FS-7 days
67	Cor balok B4c 200 x 400 f <sub>c</sub> = 2	14 days	Fri 05/10/18	Thu 18/10/18	66SS
68	Cor balok B8 250 x 250 f <sub>c</sub> = 25	14 days	Fri 05/10/18	Thu 18/10/18	66SS
69	Cor plat lantai A2 t. 140 mm f <sub>c</sub> =	14 days	Fri 28/09/18	Thu 11/10/18	65SS+7 days
70	<b>PEKERJAAN ARSITEKTUR</b>	<b>196 days</b>	<b>Fri 06/07/18</b>	<b>Thu 17/01/19</b>	
71	<b>PEKERJAAN GALIAN DAN URUGAN</b>	<b>105 days</b>	<b>Fri 06/07/18</b>	<b>Thu 18/10/18</b>	
72	Galian pondasi batu kali 1 m	14 days	Fri 21/09/18	Thu 04/10/18	62SS
73	Urugan pasir bawah pondasi batu ka	14 days	Fri 21/09/18	Thu 04/10/18	72SS
74	Urugan pasir bawah lantai tebal = 10	7 days	Fri 28/09/18	Thu 04/10/18	72FF
75	Urugan kembali galian pondasi	7 days	Fri 28/09/18	Thu 04/10/18	74FF
76	Urugan sirtu peninggian peil bangunan	0 days	Fri 06/07/18	Fri 06/07/18	
77	Urugan Tanah Peninggian peil bangun	28 days	Fri 21/09/18	Thu 18/10/18	73SS
78	<b>PEKERJAAN BETON PRAKTIS</b>	<b>35 days</b>	<b>Fri 28/09/18</b>	<b>Thu 01/11/18</b>	
79	<b>LANTAI 1</b>	<b>28 days</b>	<b>Fri 05/10/18</b>	<b>Thu 01/11/18</b>	
80	Cor sloof praktis	14 days	Fri 05/10/18	Thu 18/10/18	73
81	Cor kolom praktis	14 days	Fri 05/10/18	Thu 18/10/18	80SS
82	Cor ring balok praktis	21 days	Fri 12/10/18	Thu 01/11/18	68FS-7 days
83	Cor balok lateui	21 days	Fri 12/10/18	Thu 01/11/18	82SS

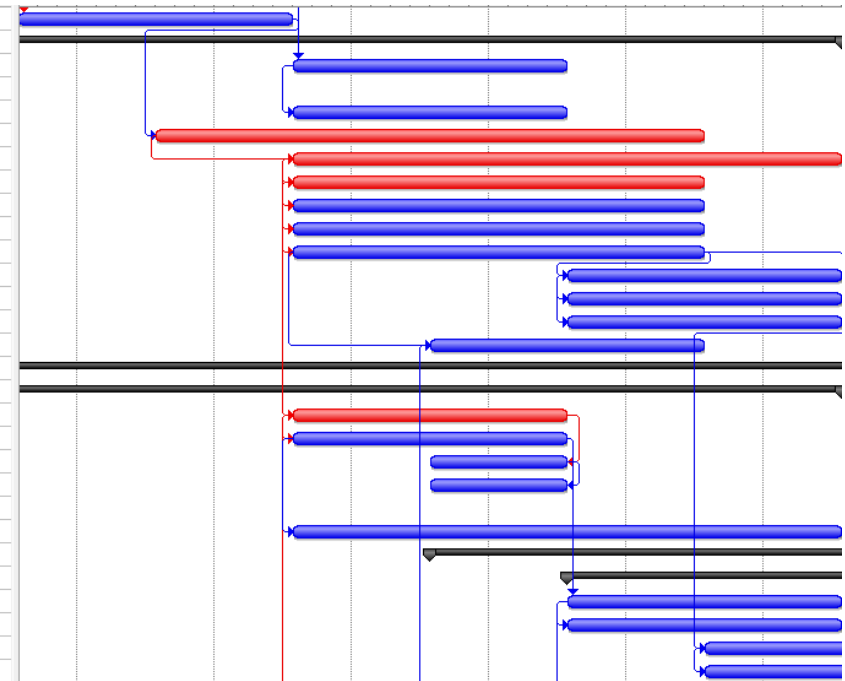


83	Cor balok lateui	21 days	Fri 12/10/18	Thu 01/11/18	82SS
84	<b>LANTAI 2</b>	<b>28 days</b>	<b>Fri 28/09/18</b>	<b>Thu 25/10/18</b>	
85	Cor kolom praktis	14 days	Fri 28/09/18	Thu 11/10/18	69SS
86	Cor ring balok praktis	21 days	Fri 05/10/18	Thu 25/10/18	80SS
87	Cor balok lateui	21 days	Fri 05/10/18	Thu 25/10/18	86SS
88	<b>PEKERJAAN PASANGAN DAN PLESTER</b>	<b>63 days</b>	<b>Fri 21/09/18</b>	<b>Thu 22/11/18</b>	
89	<b>LANTAI 1</b>	<b>42 days</b>	<b>Fri 21/09/18</b>	<b>Thu 01/11/18</b>	
90	Pasangan pondasi batu kali 1pc	14 days	Fri 21/09/18	Thu 04/10/18	72SS
91	Pasangan dinding 1/2 bata 1pc :	21 days	Fri 28/09/18	Thu 18/10/18	90FS-7 days
92	Pasangan dinding 1/2 bata 1pc :	21 days	Fri 28/09/18	Thu 18/10/18	90FS-7 days
93	Plesteran dinding 1 pc : 6 ps	21 days	Fri 28/09/18	Thu 18/10/18	91SS
94	Plesteran dinding 1 pc : 3 ps	21 days	Fri 05/10/18	Thu 25/10/18	93SS+7 days
95	Pasangan batu alam andesit	21 days	Fri 05/10/18	Thu 25/10/18	93SS+7 days
96	Plester dan acian beton 1 Pc : 3	21 days	Fri 05/10/18	Thu 25/10/18	95SS
97	Plesteran tali air 1 pc : 3ps	21 days	Fri 05/10/18	Thu 25/10/18	96SS
98	Plesteran skoning 1 pc : 2 ps	21 days	Fri 05/10/18	Thu 25/10/18	97SS
99	Wall filler plat tangga	21 days	Fri 05/10/18	Thu 25/10/18	98SS
100	Plesteran penebalan dinding	21 days	Fri 05/10/18	Thu 25/10/18	99SS
101	Acian dinding	21 days	Fri 12/10/18	Thu 01/11/18	93FS-7 days
102	Cor plat meja beton tebal 100 mr	21 days	Fri 12/10/18	Thu 01/11/18	101SS
103	Cor plat topi tebal 100 mm	21 days	Fri 12/10/18	Thu 01/11/18	102SS
104	Plester dan acian beton 1 Pc : 3	21 days	Fri 12/10/18	Thu 01/11/18	103SS
105	Plester dan acian beton 1 Pc : 3	21 days	Fri 12/10/18	Thu 01/11/18	104SS
106	<b>LANTAI 2</b>	<b>49 days</b>	<b>Fri 05/10/18</b>	<b>Thu 22/11/18</b>	
107	Pasangan dinding 1/2 bata 1pc :	28 days	Fri 05/10/18	Thu 01/11/18	91SS+7 days
108	Pasangan dinding 1/2 bata 1pc :	28 days	Fri 05/10/18	Thu 01/11/18	107SS
109	Plesteran dinding 1 pc : 6 ps	14 days	Fri 26/10/18	Thu 08/11/18	107FS-7 days
110	Plesteran dinding 1 pc : 3 ps	14 days	Fri 26/10/18	Thu 08/11/18	109SS

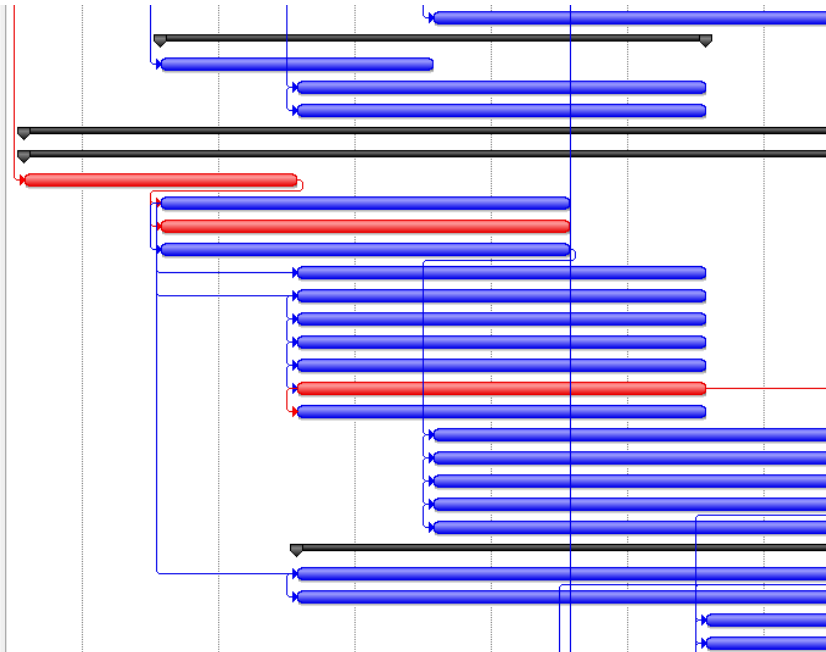


110	Plesteran dinding 1 pc : 3 ps	14 days	Fri 26/10/18	Thu 08/11/18	109SS
111	Plester dan acian beton 1 Pc : 3	14 days	Fri 26/10/18	Thu 08/11/18	110SS
112	Plesteran tali air 1 pc : 3ps	14 days	Fri 26/10/18	Thu 08/11/18	111SS
113	Plesteran skoning 1 pc : 2 ps	14 days	Fri 26/10/18	Thu 08/11/18	112SS
114	Plesteran profil 1 pc : 2 ps	14 days	Fri 26/10/18	Thu 08/11/18	113SS
115	Plesteran penebalan dinding	14 days	Fri 26/10/18	Thu 08/11/18	114SS
116	Acian dinding	28 days	Fri 26/10/18	Thu 22/11/18	115SS
117	Cor plat meja beton tebal 100 mrr	21 days	Fri 26/10/18	Thu 15/11/18	104FS-7 days
118	Cor plat topi tebal 100 mm	21 days	Fri 26/10/18	Thu 15/11/18	117SS
119	Plester dan acian beton 1 Pc : 3	21 days	Fri 26/10/18	Thu 15/11/18	118SS
120	Plester dan acian beton 1 Pc : 3	21 days	Fri 26/10/18	Thu 15/11/18	119SS
121	Screeding plat lantai	21 days	Fri 26/10/18	Thu 15/11/18	120SS
122	<b>LANTAI ATAP</b>	<b>7 days</b>	<b>Fri 19/10/18</b>	<b>Thu 25/10/18</b>	
123	Pasangan dinding 1/2 bata 1pc :	7 days	Fri 19/10/18	Thu 25/10/18	107FS-14 days
124	Plesteran dinding 1 pc : 6 ps	7 days	Fri 19/10/18	Thu 25/10/18	123SS
125	Acian dinding	7 days	Fri 19/10/18	Thu 25/10/18	124SS
126	Screeding plat lantai	7 days	Fri 19/10/18	Thu 25/10/18	125SS
127	<b>PEKERJAAN FINISHING LANTAI DAN DIL</b>	<b>35 days</b>	<b>Fri 02/11/18</b>	<b>Thu 06/12/18</b>	
128	<b>LANTAI 1</b>	<b>35 days</b>	<b>Fri 02/11/18</b>	<b>Thu 06/12/18</b>	
129	Homogeneous tile 600 x 600 mrr	28 days	Fri 02/11/18	Thu 29/11/18	99FS+7 days
130	Homogeneous tile 600 x 600 mrr	28 days	Fri 09/11/18	Thu 06/12/18	129SS+7 days
131	Homogeneous tile plint 100 x 600	28 days	Fri 09/11/18	Thu 06/12/18	130SS
132	Homogeneous tile KM/WC 300 x	28 days	Fri 09/11/18	Thu 06/12/18	131SS
133	Homogeneous tile dinding KM/W	28 days	Fri 09/11/18	Thu 06/12/18	132SS
134	Homogeneous tile 600 x 600 mrr	28 days	Fri 09/11/18	Thu 06/12/18	133SS
135	Homogeneous tile 600 x 600 mrr	28 days	Fri 09/11/18	Thu 06/12/18	134SS
136	Homogeneous tile 600 x 600 mrr	28 days	Fri 09/11/18	Thu 06/12/18	135SS
137	Stepnosing 100 x 600 mm (tang	28 days	Fri 09/11/18	Thu 06/12/18	136SS

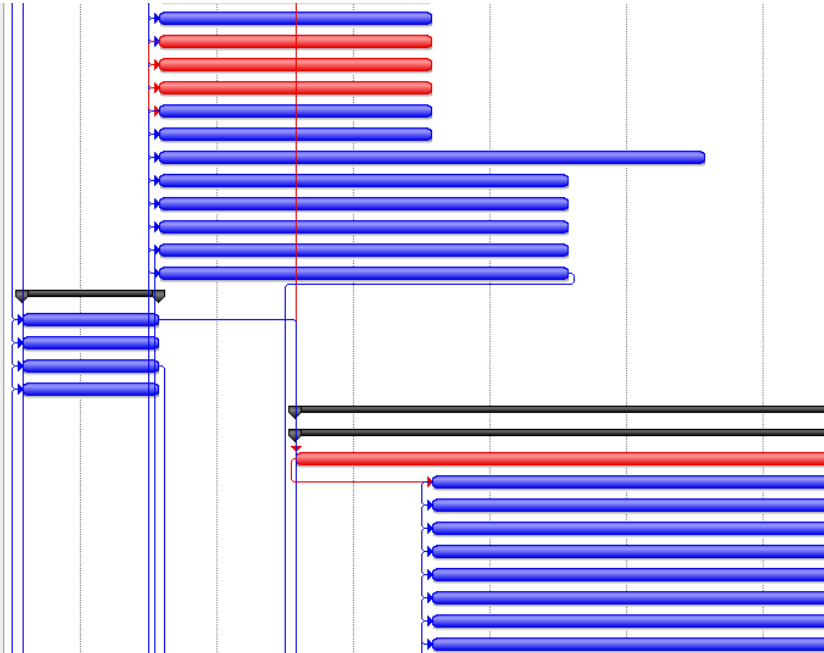


137	Stepnosing 100 x 600 mm (tangi)	28 days	Fri 09/11/18	Thu 06/12/18	136SS
138	<b>LANTAI 2</b>	<b>28 days</b>	<b>Fri 02/11/18</b>	<b>Thu 29/11/18</b>	
139	Homogeneous tile 600 x 600 mm	28 days	Fri 02/11/18	Thu 29/11/18	121FS-14 days
140	Homogeneous tile 600 x 600 mm	28 days	Fri 02/11/18	Thu 29/11/18	139SS
141	Homogeneous tile plint 100 x 600	28 days	Fri 02/11/18	Thu 29/11/18	140SS
142	Homogeneous tile KM/WC 300 x	21 days	Fri 09/11/18	Thu 29/11/18	141SS+7 days
143	Homogeneous tile dinding KM/W	21 days	Fri 09/11/18	Thu 29/11/18	142SS
144	Homogeneous tile 600 x 600 mm	21 days	Fri 09/11/18	Thu 29/11/18	143SS
145	<b>PEKERJAAN PINTU DAN JENDELA</b>	<b>14 days</b>	<b>Fri 09/11/18</b>	<b>Thu 22/11/18</b>	
146	<b>LANTAI 1</b>	<b>14 days</b>	<b>Fri 09/11/18</b>	<b>Thu 22/11/18</b>	
147	Pintu PU	14 days	Fri 09/11/18	Thu 22/11/18	136SS
148	Pintu P1	14 days	Fri 09/11/18	Thu 22/11/18	147SS
149	Pintu P2	14 days	Fri 09/11/18	Thu 22/11/18	148SS
150	Pintu P3	14 days	Fri 09/11/18	Thu 22/11/18	149SS
151	Pintu P4	14 days	Fri 09/11/18	Thu 22/11/18	150SS
152	Pintu PSH	14 days	Fri 09/11/18	Thu 22/11/18	151SS
153	Jendela J1	14 days	Fri 09/11/18	Thu 22/11/18	152SS
154	Jendela J2	14 days	Fri 09/11/18	Thu 22/11/18	153SS
155	Jendela J3	14 days	Fri 09/11/18	Thu 22/11/18	154SS
156	Jendela J4	14 days	Fri 09/11/18	Thu 22/11/18	155SS
157	Boven BV1	14 days	Fri 09/11/18	Thu 22/11/18	156SS
158	Boven BV2	14 days	Fri 09/11/18	Thu 22/11/18	157SS
159	Glass Block GB1	14 days	Fri 09/11/18	Thu 22/11/18	158SS
160	<b>LANTAI 2</b>	<b>14 days</b>	<b>Fri 09/11/18</b>	<b>Thu 22/11/18</b>	
161	Pintu P1	14 days	Fri 09/11/18	Thu 22/11/18	144SS
162	Pintu P2	14 days	Fri 09/11/18	Thu 22/11/18	161SS
163	Pintu P3	14 days	Fri 09/11/18	Thu 22/11/18	162SS
164	Pintu PSH	14 days	Fri 09/11/18	Thu 22/11/18	163SS

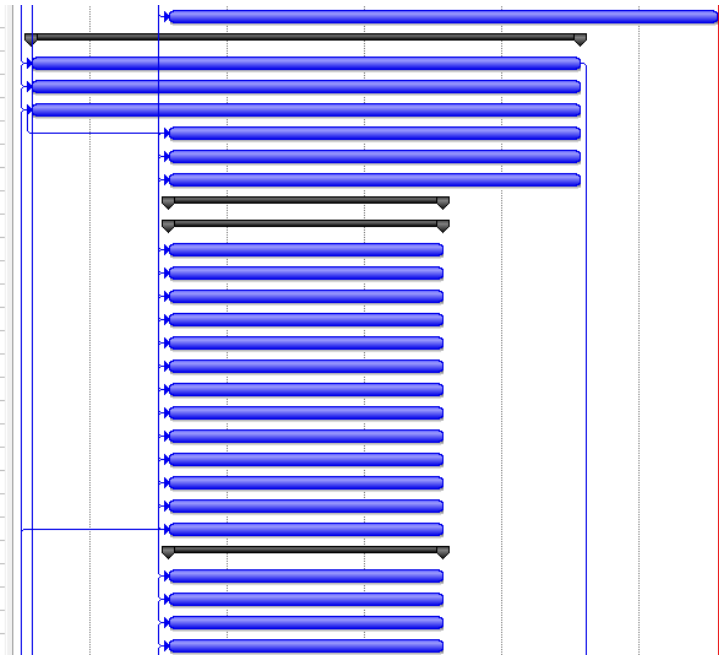

164	Pintu PSH	14 days	Fri 09/11/18	Thu 22/11/18	163SS
165	Jendela J1	14 days	Fri 09/11/18	Thu 22/11/18	164SS
166	Jendela J2	14 days	Fri 09/11/18	Thu 22/11/18	165SS
167	Jendela J5	14 days	Fri 09/11/18	Thu 22/11/18	166SS
168	Jendela J6	14 days	Fri 09/11/18	Thu 22/11/18	167SS
169	Jendela J7	14 days	Fri 09/11/18	Thu 22/11/18	168SS
170	Boven BV1	14 days	Fri 09/11/18	Thu 22/11/18	169SS
171	<input type="checkbox"/> PEKERJAAN PARTISI	35 days	Fri 19/10/18	Thu 22/11/18	
172	<input type="checkbox"/> LANTAI 1	21 days	Fri 19/10/18	Thu 08/11/18	
173	Partisi PR1	14 days	Fri 19/10/18	Thu 01/11/18	126SS
174	Partisi PR2	14 days	Fri 19/10/18	Thu 01/11/18	173SS
175	Partisi PR3	14 days	Fri 19/10/18	Thu 01/11/18	174SS
176	Partisi PR4	14 days	Fri 19/10/18	Thu 01/11/18	175SS
177	Partisi PR5	14 days	Fri 26/10/18	Thu 08/11/18	173FS-7 days
178	Partisi PR6	14 days	Fri 26/10/18	Thu 08/11/18	177SS
179	Partisi PR7	14 days	Fri 26/10/18	Thu 08/11/18	178SS
180	Partisi PR8	14 days	Fri 26/10/18	Thu 08/11/18	179SS
181	Partisi PR9	7 days	Fri 02/11/18	Thu 08/11/18	159SS-7 days
182	Partisi PK1	7 days	Fri 02/11/18	Thu 08/11/18	181SS
183	Partisi PK2	7 days	Fri 02/11/18	Thu 08/11/18	182SS
184	Partisi PK3	7 days	Fri 02/11/18	Thu 08/11/18	183SS
185	<input type="checkbox"/> LANTAI 2	21 days	Fri 02/11/18	Thu 22/11/18	
186	Partisi PR7	7 days	Fri 02/11/18	Thu 08/11/18	141SS
187	Partisi PR10	21 days	Fri 02/11/18	Thu 22/11/18	186SS
188	Partisi PR11	21 days	Fri 02/11/18	Thu 22/11/18	187SS

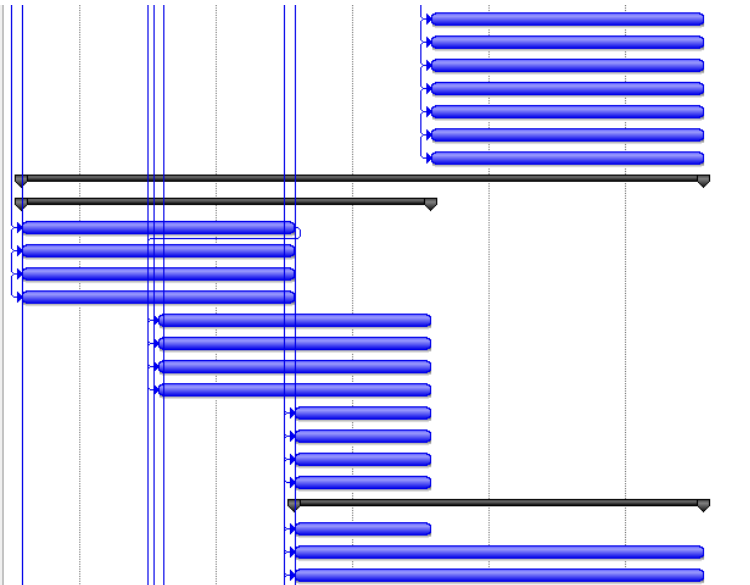


188	Partisi PR11	21 days	Fri 02/11/18	Thu 22/11/18	187SS
189	Partisi PR12	21 days	Fri 02/11/18	Thu 22/11/18	188SS
190	PEKERJAAN PLAFON	70 days	Fri 26/10/18	Thu 03/01/19	
191	LANTAI 1	63 days	Fri 02/11/18	Thu 03/01/19	
192	Plafon gypsum t = 9 mm, rangka	28 days	Fri 02/11/18	Thu 29/11/18	123FS+7 days
193	List plafon shadow line	28 days	Fri 30/11/18	Thu 27/12/18	192
194	Maintenance hole	7 days	Fri 28/12/18	Thu 03/01/19	193
195	LANTAI 2	49 days	Fri 26/10/18	Thu 13/12/18	
196	Plafon gypsum t = 9 mm, rangka	28 days	Fri 26/10/18	Thu 22/11/18	116SS
197	Plafon gypsum t = 9 mm, rangka	28 days	Fri 02/11/18	Thu 29/11/18	120SS+7 days
198	Plafon kalsium silikat t = 6 mm, rangka	28 days	Fri 02/11/18	Thu 29/11/18	141SS
199	List plafon shadow line	28 days	Fri 09/11/18	Thu 06/12/18	189SS+7 days
200	Maintenance hole	7 days	Fri 07/12/18	Thu 13/12/18	199
201	PEKERJAAN PENGECATAN	84 days	Fri 26/10/18	Thu 17/01/19	
202	LANTAI 1	42 days	Fri 07/12/18	Thu 17/01/19	
203	Cat dinding luar	28 days	Fri 07/12/18	Thu 03/01/19	129FS+7 days
204	Cat dinding dalam (dinding, kolor)	21 days	Fri 28/12/18	Thu 17/01/19	203FS-7 days
205	Cat Plafon	21 days	Fri 28/12/18	Thu 17/01/19	204SS
206	Cat batu alam	21 days	Fri 28/12/18	Thu 17/01/19	205SS
207	Cat lisplank beton	21 days	Fri 28/12/18	Thu 17/01/19	206SS
208	Cat plat topi	21 days	Fri 28/12/18	Thu 17/01/19	207SS
209	LANTAI 2	14 days	Fri 30/11/18	Thu 13/12/18	
210	Cat dinding luar (dinding, kolom)	14 days	Fri 30/11/18	Thu 13/12/18	139
211	Cat dinding dalam (dinding, kolor)	14 days	Fri 30/11/18	Thu 13/12/18	210SS
212	Cat lisplank beton	7 days	Fri 07/12/18	Thu 13/12/18	210FS-7 days
213	Cat Plafon	7 days	Fri 07/12/18	Thu 13/12/18	212SS
214	Cat plat topi	7 days	Fri 07/12/18	Thu 13/12/18	213SS
215	Waterproofing plat	7 days	Fri 07/12/18	Thu 13/12/18	214SS

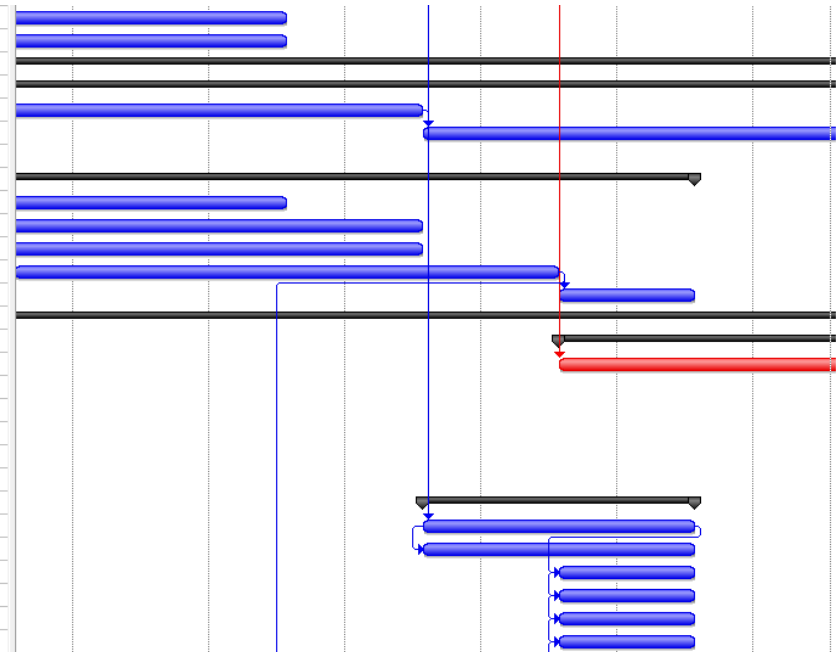




215	Waterproofing plat	7 days	Fri 07/12/18	Thu 13/12/18	214SS
216	Waterproofing km/wc	7 days	Fri 07/12/18	Thu 13/12/18	215SS
217	<b>☐ LANTAI ATAP</b>	<b>21 days</b>	<b>Fri 26/10/18</b>	<b>Thu 15/11/18</b>	
218	Cat dinding luar (dinding, kolom)	21 days	Fri 26/10/18	Thu 15/11/18	125
219	Waterproofing plat	21 days	Fri 26/10/18	Thu 15/11/18	218SS
220	<b>☐ PEKERJAAN ATAP</b>	<b>21 days</b>	<b>Fri 19/10/18</b>	<b>Thu 08/11/18</b>	
221	Rangka atap baja ringan	21 days	Fri 19/10/18	Thu 08/11/18	65FS+7 days
222	Aluminium foil single side jenis wove	21 days	Fri 19/10/18	Thu 08/11/18	221SS
223	Penutup atap genteng keramik	21 days	Fri 19/10/18	Thu 08/11/18	222SS
224	Bubungan atap	21 days	Fri 19/10/18	Thu 08/11/18	223SS
225	Bubungan penutup	21 days	Fri 19/10/18	Thu 08/11/18	224SS
226	Bubungan 3 arah	21 days	Fri 19/10/18	Thu 08/11/18	225SS
227	Lisplank woodplank 2 x 0.8 x 20 cm	21 days	Fri 19/10/18	Thu 08/11/18	226SS
228	<b>☐ PEKERJAAN FINISHING EXTERIOR</b>	<b>7 days</b>	<b>Fri 26/10/18</b>	<b>Thu 01/11/18</b>	
229	Pasangan GRC + rangka uk. 1200 x 500	7 days	Fri 26/10/18	Thu 01/11/18	219SS
230	Pasangan GRC + rangka uk. 800 x 400	7 days	Fri 26/10/18	Thu 01/11/18	229SS
231	Title building "DINAS KESEHATAN" tir	7 days	Fri 26/10/18	Thu 01/11/18	230SS
232	Title building "KAB. KULON PROGO" tir	7 days	Fri 26/10/18	Thu 01/11/18	231SS
233	Mainan beton 100 mm	7 days	Fri 26/10/18	Thu 01/11/18	232SS
234	<b>☐ PEKERJAAN RAILING</b>	<b>7 days</b>	<b>Fri 06/07/18</b>	<b>Thu 12/07/18</b>	
235	Pekejaan railing tangga	7 days	Fri 06/07/18	Thu 12/07/18	
236	Pekejaan railing ramp lantai 1	7 days	Fri 06/07/18	Thu 12/07/18	
237	Pekejaan hand rail tangga	7 days	Fri 06/07/18	Thu 12/07/18	
238	<b>☐ PEKERJAAN INTERIOR</b>	<b>7 days</b>	<b>Fri 26/10/18</b>	<b>Thu 01/11/18</b>	
239	Pekerjaan meja front office	7 days	Fri 26/10/18	Thu 01/11/18	233SS
240	Pekerjaan backdrop	7 days	Fri 26/10/18	Thu 01/11/18	239SS

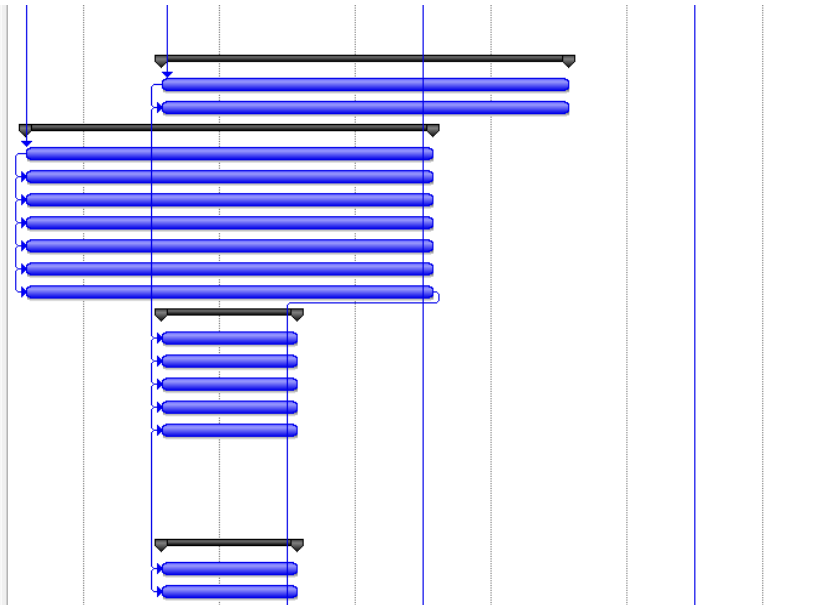


304	PEKERJAAN PENARIKAN KABEL	175 days	Fri 06/07/18	Thu 27/12/18	
305	Penarikan Kabel dari:	14 days	Fri 06/07/18	Thu 19/07/18	
306	KWH PLN ke Panel MD	14 days	Fri 06/07/18	Thu 19/07/18	244SS
307	Genset ke Panel MDP	14 days	Fri 06/07/18	Thu 19/07/18	306SS
308	Panel MDP ke SDP Pen	14 days	Fri 06/07/18	Thu 19/07/18	307SS
309	Panel MDP ke SDP Pen	14 days	Fri 06/07/18	Thu 19/07/18	308SS
310	Panel MDP ke Pompa a	14 days	Fri 06/07/18	Thu 19/07/18	309SS
311	Panel MDP ke SDP AC	14 days	Fri 06/07/18	Thu 19/07/18	399SS
312	Panel MDP ke SDP AC	14 days	Fri 06/07/18	Thu 19/07/18	400SS
313	PEKERJAAN INSTALASI LANTAI	175 days	Fri 06/07/18	Thu 27/12/18	
314	LANTAI 1	28 days	Fri 06/07/18	Thu 02/08/18	
315	Instalasi penerang	28 days	Fri 06/07/18	Thu 02/08/18	
316	Instalasi kotak kor	28 days	Fri 06/07/18	Thu 02/08/18	
317	Instalasi exhaust	14 days	Fri 06/07/18	Thu 19/07/18	
318	Exhaust Fan Siroc	21 days	Fri 06/07/18	Thu 26/07/18	
319	RMI TL LED T8 2 >	21 days	Fri 06/07/18	Thu 26/07/18	
320	Downlight 6" LED	21 days	Fri 06/07/18	Thu 26/07/18	
321	Downlight 6" LED	21 days	Fri 06/07/18	Thu 26/07/18	
322	RMI TL LED T8 2 >	21 days	Fri 06/07/18	Thu 26/07/18	
323	Pipa PVC exhaust	21 days	Fri 06/07/18	Thu 26/07/18	
324	Saklar Ganda	21 days	Fri 06/07/18	Thu 26/07/18	
325	Saklar Tunggal	21 days	Fri 06/07/18	Thu 26/07/18	
326	Kotak Kontak 500	21 days	Fri 06/07/18	Thu 26/07/18	
327	LANTAI 2	49 days	Fri 09/11/18	Thu 27/12/18	
328	Instalasi penerang	28 days	Fri 09/11/18	Thu 06/12/18	199SS
329	Instalasi kotak kor	21 days	Fri 23/11/18	Thu 13/12/18	199FS-14 days



330		Instalasi exhaust	28 days	Fri 30/11/18	Thu 27/12/18	329FS-14 days
331		Exhaust Fan Siroc	28 days	Fri 23/11/18	Thu 20/12/18	329SS
332		RMI TL LED T8 2 >	28 days	Fri 23/11/18	Thu 20/12/18	331SS
333		Downlight 6" LED	28 days	Fri 23/11/18	Thu 20/12/18	332SS
334		RMI TL LED T8 2 >	28 days	Fri 23/11/18	Thu 20/12/18	333SS
335		Downlight 6" LED	28 days	Fri 23/11/18	Thu 20/12/18	334SS
336		Pipa PVC exhaust	28 days	Fri 23/11/18	Thu 20/12/18	335SS
337		Saklar Tunggal	28 days	Fri 23/11/18	Thu 20/12/18	336SS
338		Saklar Ganda	28 days	Fri 23/11/18	Thu 20/12/18	337SS
339		Kotak Kontak 500	28 days	Fri 23/11/18	Thu 20/12/18	338SS
340		Testing and Comm	28 days	Fri 23/11/18	Thu 20/12/18	339SS
341		<b>PEKERJAAN TELEPON</b>	<b>7 days</b>	<b>Fri 06/07/18</b>	<b>Thu 12/07/18</b>	
342		<b>PERALATAN UTAMA</b>	<b>7 days</b>	<b>Fri 06/07/18</b>	<b>Thu 12/07/18</b>	
343		PABX / Key Telep	7 days	Fri 06/07/18	Thu 12/07/18	315SS
344		MDF telephone	7 days	Fri 06/07/18	Thu 12/07/18	343SS
345		Perijinan	7 days	Fri 06/07/18	Thu 12/07/18	344SS
346		Grounding	7 days	Fri 06/07/18	Thu 12/07/18	345SS
347		Testing and Comm	7 days	Fri 06/07/18	Thu 12/07/18	346SS
348		<b>KABEL FEEDER</b>	<b>133 days</b>	<b>Fri 06/07/18</b>	<b>Thu 15/11/18</b>	
349		<b>Kabel ITC 2 x 2 x 0.6</b>	<b>133 days</b>	<b>Fri 06/07/18</b>	<b>Thu 15/11/18</b>	
350		MDF telepon ke Tr	14 days	Fri 13/07/18	Thu 26/07/18	312FS-7 days
351		MDF telepon ke Tr	14 days	Fri 13/07/18	Thu 26/07/18	350SS
352		<b>LANTAI 1</b>	<b>14 days</b>	<b>Fri 13/07/18</b>	<b>Thu 26/07/18</b>	
353		Peralatan uta	0 days	Fri 13/07/18	Fri 13/07/18	351SS
354		Telephone Tr	14 days	Fri 13/07/18	Thu 26/07/18	353SS
355		Instalasi titik l	14 days	Fri 13/07/18	Thu 26/07/18	354SS
356		Outlet telpon	14 days	Fri 13/07/18	Thu 26/07/18	355SS

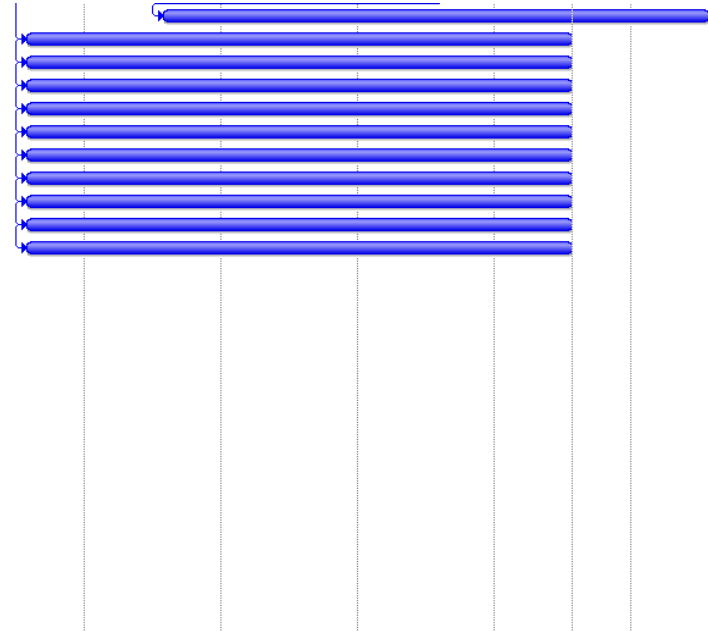


356		Outlet telpon	14 days	Fri 13/07/18	Thu 26/07/18	355SS	
357		Telephone	14 days	Fri 13/07/18	Thu 26/07/18	356SS	
358		▣ LANTAI 2	14 days	Fri 13/07/18	Thu 26/07/18		
359		Peralatan uta	0 days	Fri 13/07/18	Fri 13/07/18	351SS	
360		Telephone Tr	14 days	Fri 13/07/18	Thu 26/07/18	359SS	
361		Instalasi titik l	14 days	Fri 13/07/18	Thu 26/07/18	360SS	
362		Outlet telpon	14 days	Fri 13/07/18	Thu 26/07/18	361SS	
363		Telephone	14 days	Fri 13/07/18	Thu 26/07/18	362SS	
364		▣ PEKERJAAN LAN	14 days	Fri 13/07/18	Thu 26/07/18		
365		Instalasi kota	14 days	Fri 13/07/18	Thu 26/07/18	312FS-7 days	
366		Stop Kontak	14 days	Fri 13/07/18	Thu 26/07/18	365SS	
367		OTB	14 days	Fri 13/07/18	Thu 26/07/18	366SS	
368		Testing kone	14 days	Fri 13/07/18	Thu 26/07/18	367SS	
369		▣ KABEL FEEDER	133 days	Fri 06/07/18	Thu 15/11/18		
370		▣ Penarikan t	14 days	Fri 06/07/18	Thu 19/07/18		
371		Switch l	14 days	Fri 06/07/18	Thu 19/07/18	237SS	
372		Switch l	14 days	Fri 06/07/18	Thu 19/07/18	371SS	
373		▣ LANTAI 1	14 days	Fri 06/07/18	Thu 19/07/18		
374		Instalasi	14 days	Fri 06/07/18	Thu 19/07/18	315SS	
375		Access	14 days	Fri 06/07/18	Thu 19/07/18	374SS	
376		Outlet L	14 days	Fri 06/07/18	Thu 19/07/18	375SS	
377		▣ LANTAI 2	14 days	Fri 02/11/18	Thu 15/11/18		
378		Instalasi	14 days	Fri 02/11/18	Thu 15/11/18	227FS-7 days	
379		Access	14 days	Fri 02/11/18	Thu 15/11/18	378SS	
380		Outlet L	14 days	Fri 02/11/18	Thu 15/11/18	379SS	
381		▣ PEKERJAAN TAT	133 days	Fri 06/07/18	Thu 15/11/18		
382		▣ KABEL FEED	7 days	Fri 20/07/18	Thu 26/07/18		
383		▣ Penari	7 days	Fri 20/07/18	Thu 26/07/18		

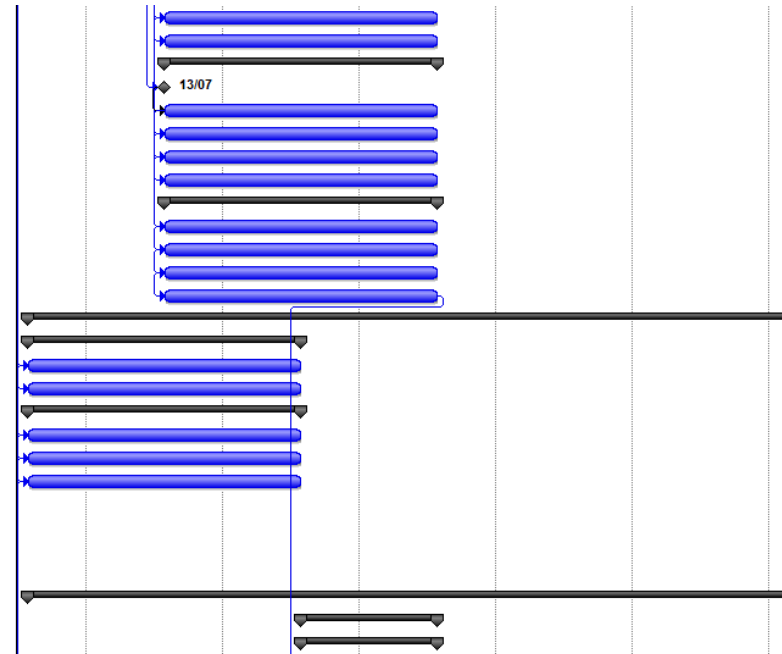


383		Penarik	7 days	Fri 20/07/18	Thu 26/07/18	
384		Po\	7 days	Fri 20/07/18	Thu 26/07/18	368FS-7 days
385		Po\	7 days	Fri 20/07/18	Thu 26/07/18	384SS
386		LANTAI 1	21 days	Fri 06/07/18	Thu 26/07/18	
387		Instalasi	14 days	Fri 06/07/18	Thu 19/07/18	376SS
388		Instalasi	14 days	Fri 06/07/18	Thu 19/07/18	387SS
389		Sound t	7 days	Fri 20/07/18	Thu 26/07/18	384SS
390		Attenua	7 days	Fri 20/07/18	Thu 26/07/18	389SS
391		Ceiling S	7 days	Fri 20/07/18	Thu 26/07/18	390SS
392		LANTAI 2	119 days	Fri 20/07/18	Thu 15/11/18	
393		Instalasi	14 days	Fri 02/11/18	Thu 15/11/18	380SS
394		Instalasi	14 days	Fri 02/11/18	Thu 15/11/18	393SS
395		Sound t	7 days	Fri 20/07/18	Thu 26/07/18	385SS
396		Attenua	7 days	Fri 20/07/18	Thu 26/07/18	395SS
397		Ceiling S	7 days	Fri 20/07/18	Thu 26/07/18	396SS
398		Testing	7 days	Fri 20/07/18	Thu 26/07/18	397SS
399		PEKERJAAN FIRE	21 days	Fri 06/07/18	Thu 26/07/18	
400		PERALATAN	7 days	Fri 06/07/18	Thu 12/07/18	
401		Master c	7 days	Fri 06/07/18	Thu 12/07/18	
402		Installat	7 days	Fri 06/07/18	Thu 12/07/18	
403		Material	0 days	Fri 06/07/18	Fri 06/07/18	
404		Testing	7 days	Fri 06/07/18	Thu 12/07/18	
405		LANTAI 1	7 days	Fri 20/07/18	Thu 26/07/18	
406		Manual t	7 days	Fri 20/07/18	Thu 26/07/18	391SS
407		Horn Str	7 days	Fri 20/07/18	Thu 26/07/18	406SS
408		Termina	7 days	Fri 20/07/18	Thu 26/07/18	407SS
409		Smoke L	7 days	Fri 20/07/18	Thu 26/07/18	408SS
410		Instalasi	7 days	Fri 20/07/18	Thu 26/07/18	409SS




411	Instalasi	7 days	Fri 20/07/18	Thu 26/07/18	410SS
412	▣ LANTAI 2	7 days	Fri 20/07/18	Thu 26/07/18	
413	Manual t	7 days	Fri 20/07/18	Thu 26/07/18	398SS
414	Horn Str	7 days	Fri 20/07/18	Thu 26/07/18	413SS
415	Termina	7 days	Fri 20/07/18	Thu 26/07/18	414SS
416	Smoke L	7 days	Fri 20/07/18	Thu 26/07/18	415SS
417	Instalasi	7 days	Fri 20/07/18	Thu 26/07/18	416SS
418	Instalasi	7 days	Fri 20/07/18	Thu 26/07/18	417SS
419	▣ PEKERJAAN KAE	14 days	Fri 06/07/18	Thu 19/07/18	
420	▣ LANTAI 1	7 days	Fri 06/07/18	Thu 12/07/18	
421	Kabel tri	7 days	Fri 06/07/18	Thu 12/07/18	387SS
422	Tee tray	7 days	Fri 06/07/18	Thu 12/07/18	421SS
423	El bow t	7 days	Fri 06/07/18	Thu 12/07/18	422SS
424	Kabel la	7 days	Fri 06/07/18	Thu 12/07/18	423SS
425	▣ LANTAI 2	7 days	Fri 13/07/18	Thu 19/07/18	
426	Kabel tri	7 days	Fri 13/07/18	Thu 19/07/18	421
427	Tee tray	7 days	Fri 13/07/18	Thu 19/07/18	426SS
428	El bow t	7 days	Fri 13/07/18	Thu 19/07/18	427SS
429	Kabel la	7 days	Fri 13/07/18	Thu 19/07/18	428SS
430	▣ PEKERJAAN PEN	14 days	Fri 06/07/18	Thu 19/07/18	
431	Air terminal F	7 days	Fri 06/07/18	Thu 12/07/18	404SS
432	kabel NYY 1:	7 days	Fri 06/07/18	Thu 12/07/18	431SS
433	Connecting S	7 days	Fri 06/07/18	Thu 12/07/18	432SS
434	Schoen cabl	7 days	Fri 06/07/18	Thu 12/07/18	433SS
435	Pipa galvanis	7 days	Fri 06/07/18	Thu 12/07/18	434SS
436	Plat plendes	7 days	Fri 06/07/18	Thu 12/07/18	435SS

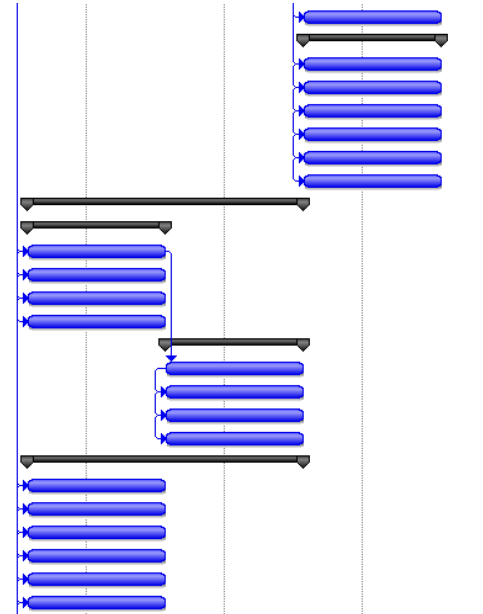

437		Kabel condu	7 days	Fri 06/07/18	Thu 12/07/18	436SS	
438		Grounding ro	7 days	Fri 06/07/18	Thu 12/07/18	437SS	
439		Pipa galvanis	7 days	Fri 06/07/18	Thu 12/07/18	438SS	
440		Splitzen temt	7 days	Fri 06/07/18	Thu 12/07/18	439SS	
441		Timah	14 days	Fri 06/07/18	Thu 19/07/18	440SS	
442		Pipa PVC 3/4	14 days	Fri 06/07/18	Thu 19/07/18	441SS	
443		Klem kabel di	14 days	Fri 06/07/18	Thu 19/07/18	442SS	
444		Pembuatan s	14 days	Fri 06/07/18	Thu 19/07/18	443SS	
445		Pembuatan b	14 days	Fri 06/07/18	Thu 19/07/18	444SS	
446		Biaya instalasi	14 days	Fri 06/07/18	Thu 19/07/18	445SS	
447		Sertifikasi da	14 days	Fri 06/07/18	Thu 19/07/18	446SS	
448		<b>PEKERJAAN GEN</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>		
449		Genset (Siler	14 days	Fri 06/07/18	Thu 19/07/18		
450		Alternator Li	0 days	Fri 06/07/18	Fri 06/07/18		
451		Control Pane	0 days	Fri 06/07/18	Fri 06/07/18		
452		Cerobong kn	14 days	Fri 06/07/18	Thu 19/07/18		
453		Testing and (	14 days	Fri 06/07/18	Thu 19/07/18		
454		<b>PEKERJAAN MEKANIKAL</b>	<b>21 days</b>	<b>Fri 06/07/18</b>	<b>Thu 26/07/18</b>		
455		<b>Instalasi air bersih</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>		
456		<b>LANTAI 1</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>		
457		Pipa suplai, PVC AW Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	312SS	
458		Pipa distribusi, PVC AW Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	457SS	
459		Pipa distribusi, PVC AW Ø 1"	14 days	Fri 06/07/18	Thu 19/07/18	458SS	
460		Pipa distribusi, PVC AW Ø 3/4"	14 days	Fri 06/07/18	Thu 19/07/18	459SS	
461		Pipa penguras , PVC AW Ø 1"	14 days	Fri 06/07/18	Thu 19/07/18	460SS	
462		Gate valve pada pipa distribusi (	14 days	Fri 06/07/18	Thu 19/07/18	461SS	
463		Pompa Transfer	14 days	Fri 06/07/18	Thu 19/07/18	462SS	
464		Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	463SS	

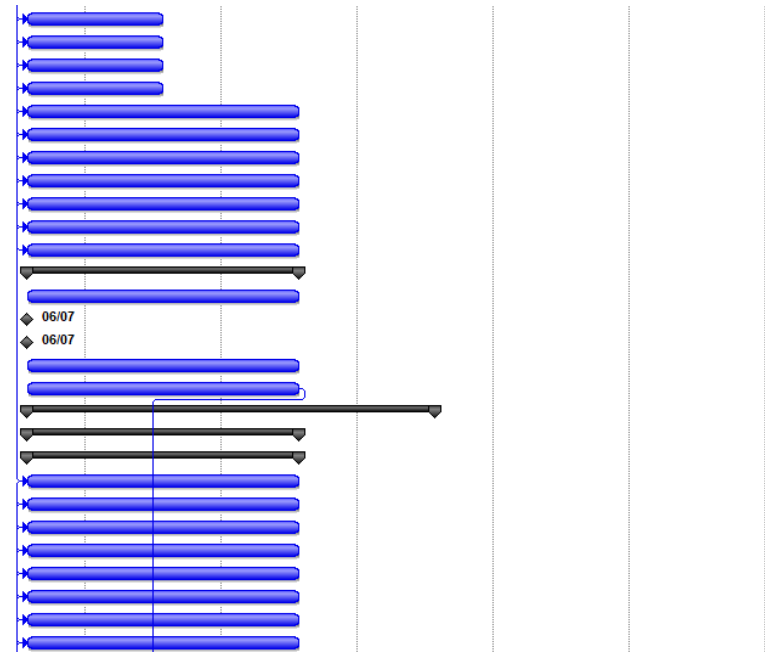

464	Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	463SS
465	Sumur + rumah pompa:	0 days	Fri 06/07/18	Fri 06/07/18	
466	Galian tanah sedalam 1 m	14 days	Fri 06/07/18	Thu 19/07/18	464SS
467	Urugan pasir bawah rumah pom	14 days	Fri 06/07/18	Thu 19/07/18	466SS
468	Cor rabat beton tebal 100 mm	14 days	Fri 06/07/18	Thu 19/07/18	467SS
469	Pasangan dinding 1/2 bata 1pcc	14 days	Fri 06/07/18	Thu 19/07/18	468SS
470	Plesteran dinding 1 pcc : 6 ps	14 days	Fri 06/07/18	Thu 19/07/18	469SS
471	Acian dinding	14 days	Fri 06/07/18	Thu 19/07/18	470SS
472	Plat baja tebal 1.2 mm penutup ri	14 days	Fri 06/07/18	Thu 19/07/18	471SS
473	Engsel	14 days	Fri 06/07/18	Thu 19/07/18	472SS
474	Pengat Ø 10 mm	14 days	Fri 06/07/18	Thu 19/07/18	473SS
475	Sumur sedalam 30 m	14 days	Fri 06/07/18	Thu 19/07/18	474SS
476	include cover pipa Ø 4"	0 days	Fri 06/07/18	Fri 06/07/18	
477	<b>LANTAI 2</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
478	Pipa suplai, PVC AW Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	457SS
479	Pipa distribusi, PVC AW Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	478SS
480	Pipa distribusi, PVC AW Ø 1"	14 days	Fri 06/07/18	Thu 19/07/18	479SS
481	Pipa distribusi, PVC AW Ø 3/4"	14 days	Fri 06/07/18	Thu 19/07/18	480SS
482	Pipa penguras , PVC AW Ø 1"	14 days	Fri 06/07/18	Thu 19/07/18	481SS
483	Gate valve pada pipa distribusi	14 days	Fri 06/07/18	Thu 19/07/18	482SS
484	Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	483SS
485	<b>LANTAI ATAP</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
486	Pipa suplai, PVC AW Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	484SS
487	Pipa distribusi, PVC AW Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	486SS
488	Pipa header, PVC AW Ø 2"	14 days	Fri 06/07/18	Thu 19/07/18	487SS
489	Pipa over flow, PVC AW Ø 1"	14 days	Fri 06/07/18	Thu 19/07/18	488SS
490	Pipa penguras, PVC AW Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	489SS
491	Gate valve pipa suplai Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	490SS

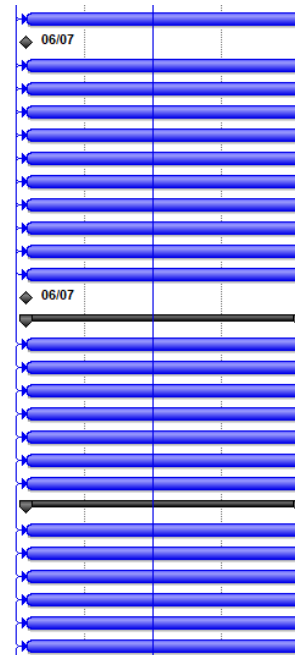




491	Gate valve pipa suplai Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	490SS
492	Gate valve pipa distribusi Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	491SS
493	Gate valve pipa over flow Ø 1"	14 days	Fri 06/07/18	Thu 19/07/18	492SS
494	Gate valve pipa penguras Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	493SS
495	Roof tank 700 L + Radar (autosv	14 days	Fri 06/07/18	Thu 19/07/18	494SS
496	Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	495SS
497	<b>Instalasi Air Bekas</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
498	<b>LANTAI 1</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
499	Pipa air bekas, PVC AW Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	496SS
500	Pipa air bekas, PVC AW Ø 2"	14 days	Fri 06/07/18	Thu 19/07/18	499SS
501	Pipa air bekas, PVC AW Ø 3"	14 days	Fri 06/07/18	Thu 19/07/18	500SS
502	Pipa air bekas, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	501SS
503	Sumur resapan air bekas	14 days	Fri 06/07/18	Thu 19/07/18	502SS
504	Bak kontrol air bekas	14 days	Fri 06/07/18	Thu 19/07/18	503SS
505	Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	504SS
506	<b>LANTAI 2</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
507	Pipa air bekas, PVC AW Ø 1 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	505SS
508	Pipa air bekas, PVC AW Ø 2"	14 days	Fri 06/07/18	Thu 19/07/18	507SS
509	Pipa air bekas, PVC AW Ø 3"	14 days	Fri 06/07/18	Thu 19/07/18	508SS
510	Pipa air bekas, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	509SS
511	Pipa air vent, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	510SS
512	Pipa vent, PVC AW Ø 3"	14 days	Fri 06/07/18	Thu 19/07/18	511SS
513	Clean Out	14 days	Fri 06/07/18	Thu 19/07/18	512SS
514	Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	513SS
515	<b>Instalasi Air Kotor</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
516	<b>LANTAI 1</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
517	Pipa air kotor, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	514SS
518	Pipa overflow, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	517SS




518	Pipa overflow, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	517SS
519	Bak kontrol air kotor	14 days	Fri 06/07/18	Thu 19/07/18	518SS
520	Sumur resapan air kotor	14 days	Fri 06/07/18	Thu 19/07/18	519SS
521	Bio Septictank 4 m3 + Rumah	14 days	Fri 06/07/18	Thu 19/07/18	520SS
522	Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	521SS
523	<b>LANTAI 2</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
524	Pipa air kotor, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	522SS
525	Pipa air vent, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	524SS
526	Clean Out	14 days	Fri 06/07/18	Thu 19/07/18	525SS
527	Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	526SS
528	<b>Instalasi Air Hujan</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
529	<b>LANTAI 1</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
530	Pipa air hujan, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	527SS
531	Saluran air, pasangan pondasi t	14 days	Fri 06/07/18	Thu 19/07/18	530SS
532	Penutup saluran	14 days	Fri 06/07/18	Thu 19/07/18	531SS
533	Saluran buis beton Ø 30 cm	14 days	Fri 06/07/18	Thu 19/07/18	532SS
534	Bak kontrol	14 days	Fri 06/07/18	Thu 19/07/18	533SS
535	Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	534SS
536	<b>LANTAI 2</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
537	Pipa air hujan, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	535SS
538	Pipa air hujan, PVC AW Ø 2"	14 days	Fri 06/07/18	Thu 19/07/18	537SS
539	Gutter	14 days	Fri 06/07/18	Thu 19/07/18	538SS
540	Roof drain	14 days	Fri 06/07/18	Thu 19/07/18	539SS
541	Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	540SS
542	<b>LANTAI ATAP</b>	<b>14 days</b>	<b>Fri 06/07/18</b>	<b>Thu 19/07/18</b>	
543	Pipa air kotor, PVC AW Ø 4"	14 days	Fri 06/07/18	Thu 19/07/18	541SS
544	Gutter	14 days	Fri 06/07/18	Thu 19/07/18	543SS
545	Roof drain	14 days	Fri 06/07/18	Thu 19/07/18	544SS



545	Roof drain	14 days	Fri 06/07/18	Thu 19/07/18	544SS	
546	Fitting + Supporting	14 days	Fri 06/07/18	Thu 19/07/18	545SS	
547	☐ Peralatan saniter	14 days	Fri 06/07/18	Thu 19/07/18		
548	☐ LANTAI 1	14 days	Fri 06/07/18	Thu 19/07/18		
549	Kran Ø 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	546SS	
550	Floordrain	14 days	Fri 06/07/18	Thu 19/07/18	549SS	
551	Kloset jongkok	14 days	Fri 06/07/18	Thu 19/07/18	550SS	
552	Wastafel + kran + cermin + akse	14 days	Fri 06/07/18	Thu 19/07/18	551SS	
553	Jet washer	14 days	Fri 06/07/18	Thu 19/07/18	552SS	
554	Kloset duduk difable	14 days	Fri 06/07/18	Thu 19/07/18	553SS	
555	Zink	14 days	Fri 06/07/18	Thu 19/07/18	554SS	
556	Pegangan stainless	14 days	Fri 06/07/18	Thu 19/07/18	555SS	
557	☐ LANTAI 2	14 days	Fri 06/07/18	Thu 19/07/18		
558	Kran Ø 1/2"	14 days	Fri 06/07/18	Thu 19/07/18	556SS	
559	Floordrain	14 days	Fri 06/07/18	Thu 19/07/18	558SS	
560	Kloset jongkok	14 days	Fri 06/07/18	Thu 19/07/18	559SS	
561	Wastafel + kran + cermin + akse	14 days	Fri 06/07/18	Thu 19/07/18	560SS	
562	Clean out	14 days	Fri 06/07/18	Thu 19/07/18	561SS	
563	☐ PEKERJAAN TATA UDARA	14 days	Fri 13/07/18	Thu 26/07/18		
564	☐ LANTAI 1	14 days	Fri 13/07/18	Thu 26/07/18		
565	Instalasi Indoor AC (NYM 3 x 2.5	14 days	Fri 13/07/18	Thu 26/07/18	453FS-7 days	
566	Stop Kontak AC	14 days	Fri 13/07/18	Thu 26/07/18	565SS	
567	Unit AC type wall split kap 3/4 PI	14 days	Fri 13/07/18	Thu 26/07/18	566SS	
568	Unit AC type wall split kap 1 PK	14 days	Fri 13/07/18	Thu 26/07/18	567SS	
569	Unit AC type wall split kap 1.5 PI	14 days	Fri 13/07/18	Thu 26/07/18	568SS	
570	Unit AC type wall split kap 2 PK	14 days	Fri 13/07/18	Thu 26/07/18	569SS	
571	Pipa refrigerant 6.35 mm + 12.7	14 days	Fri 13/07/18	Thu 26/07/18	570SS	
572	Pipa Drain AC Ø 3/4 "	14 days	Fri 13/07/18	Thu 26/07/18	571SS	

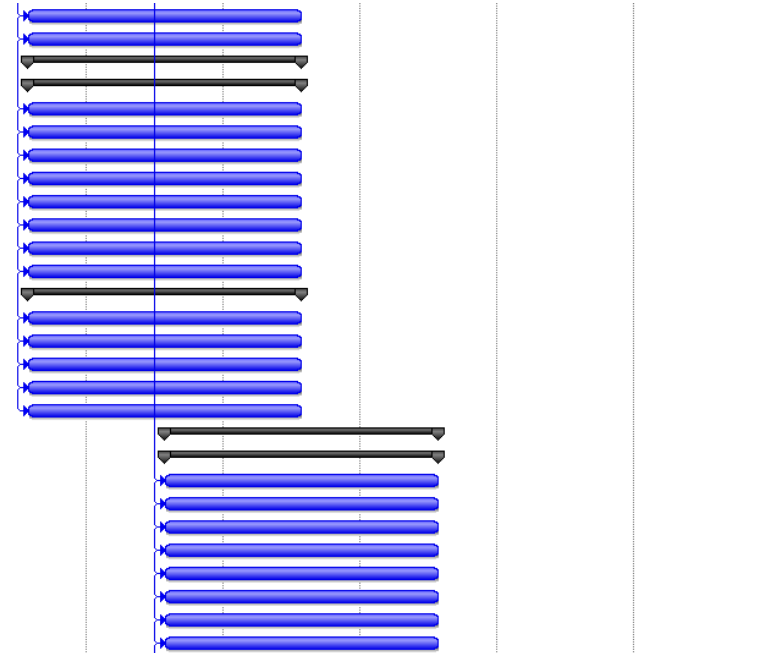

572	Pipa Drain AC Ø 3/4 "	14 days	Fri 13/07/18	Thu 26/07/18	571SS
573	<b>LANTAI 2</b>	<b>14 days</b>	<b>Fri 13/07/18</b>	<b>Thu 26/07/18</b>	
574	Instalasi Indoor AC (NYM 3 x 2.5	14 days	Fri 13/07/18	Thu 26/07/18	572SS
575	Stop Kontak AC	14 days	Fri 13/07/18	Thu 26/07/18	574SS
576	Unit AC type wall split kap 3/4 Pl	14 days	Fri 13/07/18	Thu 26/07/18	575SS
577	Unit AC type wall split kap 1 PK	14 days	Fri 13/07/18	Thu 26/07/18	576SS
578	Unit AC type wall split kap 1.5 Pl	14 days	Fri 13/07/18	Thu 26/07/18	577SS
579	Unit AC type wall split kap 2 PK	14 days	Fri 13/07/18	Thu 26/07/18	578SS
580	Pipa refrigerant 6.35 mm + 12.7	14 days	Fri 13/07/18	Thu 26/07/18	579SS
581	Pipa Drain AC Ø 3/4 "	14 days	Fri 13/07/18	Thu 26/07/18	580SS
582	<b>PEKERJAAN LANDSCAPE</b>	<b>164 days</b>	<b>Fri 06/07/18</b>	<b>Sun 16/12/18</b>	
583	<b>PEKERJAAN HARDSCAPE</b>	<b>164 days</b>	<b>Fri 06/07/18</b>	<b>Sun 16/12/18</b>	
584	Paving holland tebal 80mm, K-300	28 days	Mon 12/11/18	Sun 09/12/18	
585	Urugan sirtu peninggian peil halaman	21 days	Mon 05/11/18	Sun 25/11/18	584SS-7 days
586	Tiang bendera	7 days	Mon 03/12/18	Sun 09/12/18	584FS-7 days
587	Bak bunga	0 days	Fri 06/07/18	Fri 06/07/18	
588	Pasangan dinding 1/2 bata 1pcc : 6p	14 days	Mon 19/11/18	Sun 02/12/18	585FS-7 days
589	Plesteran dinding 1 pcc : 6 ps	14 days	Mon 26/11/18	Sun 09/12/18	588FS-7 days
590	Acian	14 days	Mon 26/11/18	Sun 09/12/18	589SS
591	Cat dinding luar	14 days	Mon 03/12/18	Sun 16/12/18	590FS-7 days
592	Pintu gerbang	7 days	Mon 10/12/18	Sun 16/12/18	591FS-7 days
593	Ramp jalan masuk	0 days	Fri 06/07/18	Fri 06/07/18	
594	Galian pondasi batu kali	14 days	Fri 06/07/18	Thu 19/07/18	
595	Urugan pasir bawah pondasi batu ka	14 days	Fri 06/07/18	Thu 19/07/18	
596	Urugan pasir bawah Ramp tebal = 10	14 days	Fri 06/07/18	Thu 19/07/18	
597	Urugan tanah kembali pondasi batu k	14 days	Fri 06/07/18	Thu 19/07/18	
598	Pasangan pondasi batu kali 1pcc : 8p	14 days	Fri 06/07/18	Thu 19/07/18	
599	Cor plat ramp tebal 120 mm, 1 pc : 2 p	14 days	Fri 06/07/18	Thu 19/07/18	

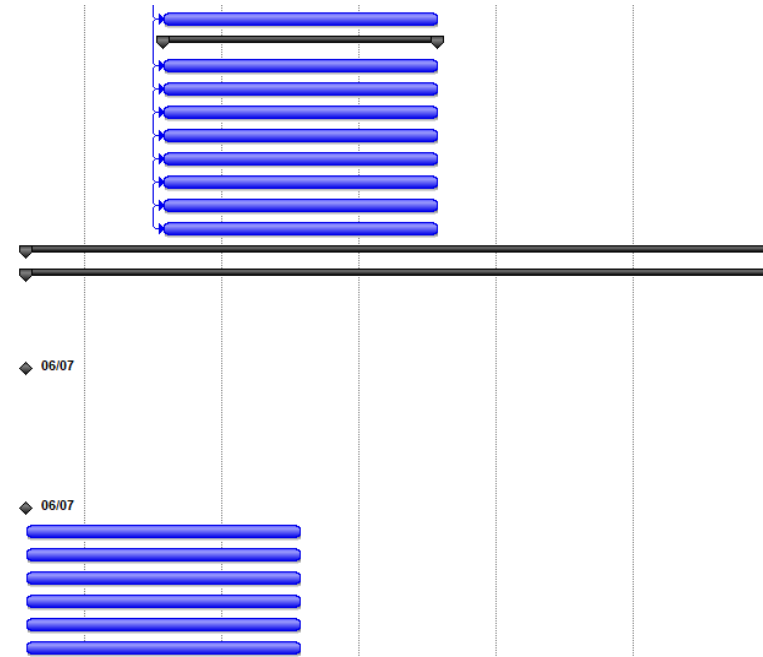

600	tul wiremesh M5-15 1 lapis	0 days	Fri 06/07/18	Fri 06/07/18
601	Finishing acian	14 days	Fri 06/07/18	Thu 19/07/18
602	<b>PEKERJAAN PAGAR</b>	<b>28 days</b>	<b>Fri 06/07/18</b>	<b>Thu 02/08/18</b>
603	<b>Pekerjaan galian dan urugan</b>	<b>28 days</b>	<b>Fri 06/07/18</b>	<b>Thu 02/08/18</b>
604	Galian pondasi batu kali, sampai	14 days	Fri 06/07/18	Thu 19/07/18
605	Urug pasir bawah pondasi batu	14 days	Fri 06/07/18	Thu 19/07/18
606	Urug tanah kembali bekas galian	28 days	Fri 06/07/18	Thu 02/08/18
607	<b>Pekerjaan beton</b>	<b>28 days</b>	<b>Fri 06/07/18</b>	<b>Thu 02/08/18</b>
608	Balok sloof praktis, uk. 120 x 20	14 days	Fri 06/07/18	Thu 19/07/18
609	Balok ring praktis, uk. 120 x 200	28 days	Fri 06/07/18	Thu 02/08/18
610	Kolom K1, uk. 400 x 400 mm (1p)	28 days	Fri 06/07/18	Thu 02/08/18
611	Kolom K2, uk. 300 x 300 mm (1p)	28 days	Fri 06/07/18	Thu 02/08/18
612	<b>Pekerjaan pasangan &amp; plesteran</b>	<b>28 days</b>	<b>Fri 06/07/18</b>	<b>Thu 02/08/18</b>
613	Pasangan pondasi batu kali (1pc)	28 days	Fri 06/07/18	Thu 02/08/18
614	Pasangan dinding 1/2 bata merah	28 days	Fri 06/07/18	Thu 02/08/18
615	Plesteran dinding 1/2 bata merah	28 days	Fri 06/07/18	Thu 02/08/18
616	Acian dinding bata merah	28 days	Fri 06/07/18	Thu 02/08/18
617	Plester dan acian beton	28 days	Fri 06/07/18	Thu 02/08/18
618	Plesteran ban-banan	28 days	Fri 06/07/18	Thu 02/08/18
619	Sponengan (1 pc : 2 ps)	28 days	Fri 06/07/18	Thu 02/08/18
620	Ornamen pada top kolom	21 days	Fri 06/07/18	Thu 26/07/18
621	<b>Pekerjaan pengecatan</b>	<b>21 days</b>	<b>Fri 06/07/18</b>	<b>Thu 26/07/18</b>
622	Cat dinding eksterior	21 days	Fri 06/07/18	Thu 26/07/18
623	Cat ornamen pada puncak kolom	21 days	Fri 06/07/18	Thu 26/07/18
624	<b>Pekerjaan title building</b>	<b>7 days</b>	<b>Fri 06/07/18</b>	<b>Thu 12/07/18</b>
625	Title building "DINAS KESEHATA	7 days	Fri 06/07/18	Thu 12/07/18
626	Title building "KAB. KULON PROI	7 days	Fri 06/07/18	Thu 12/07/18

