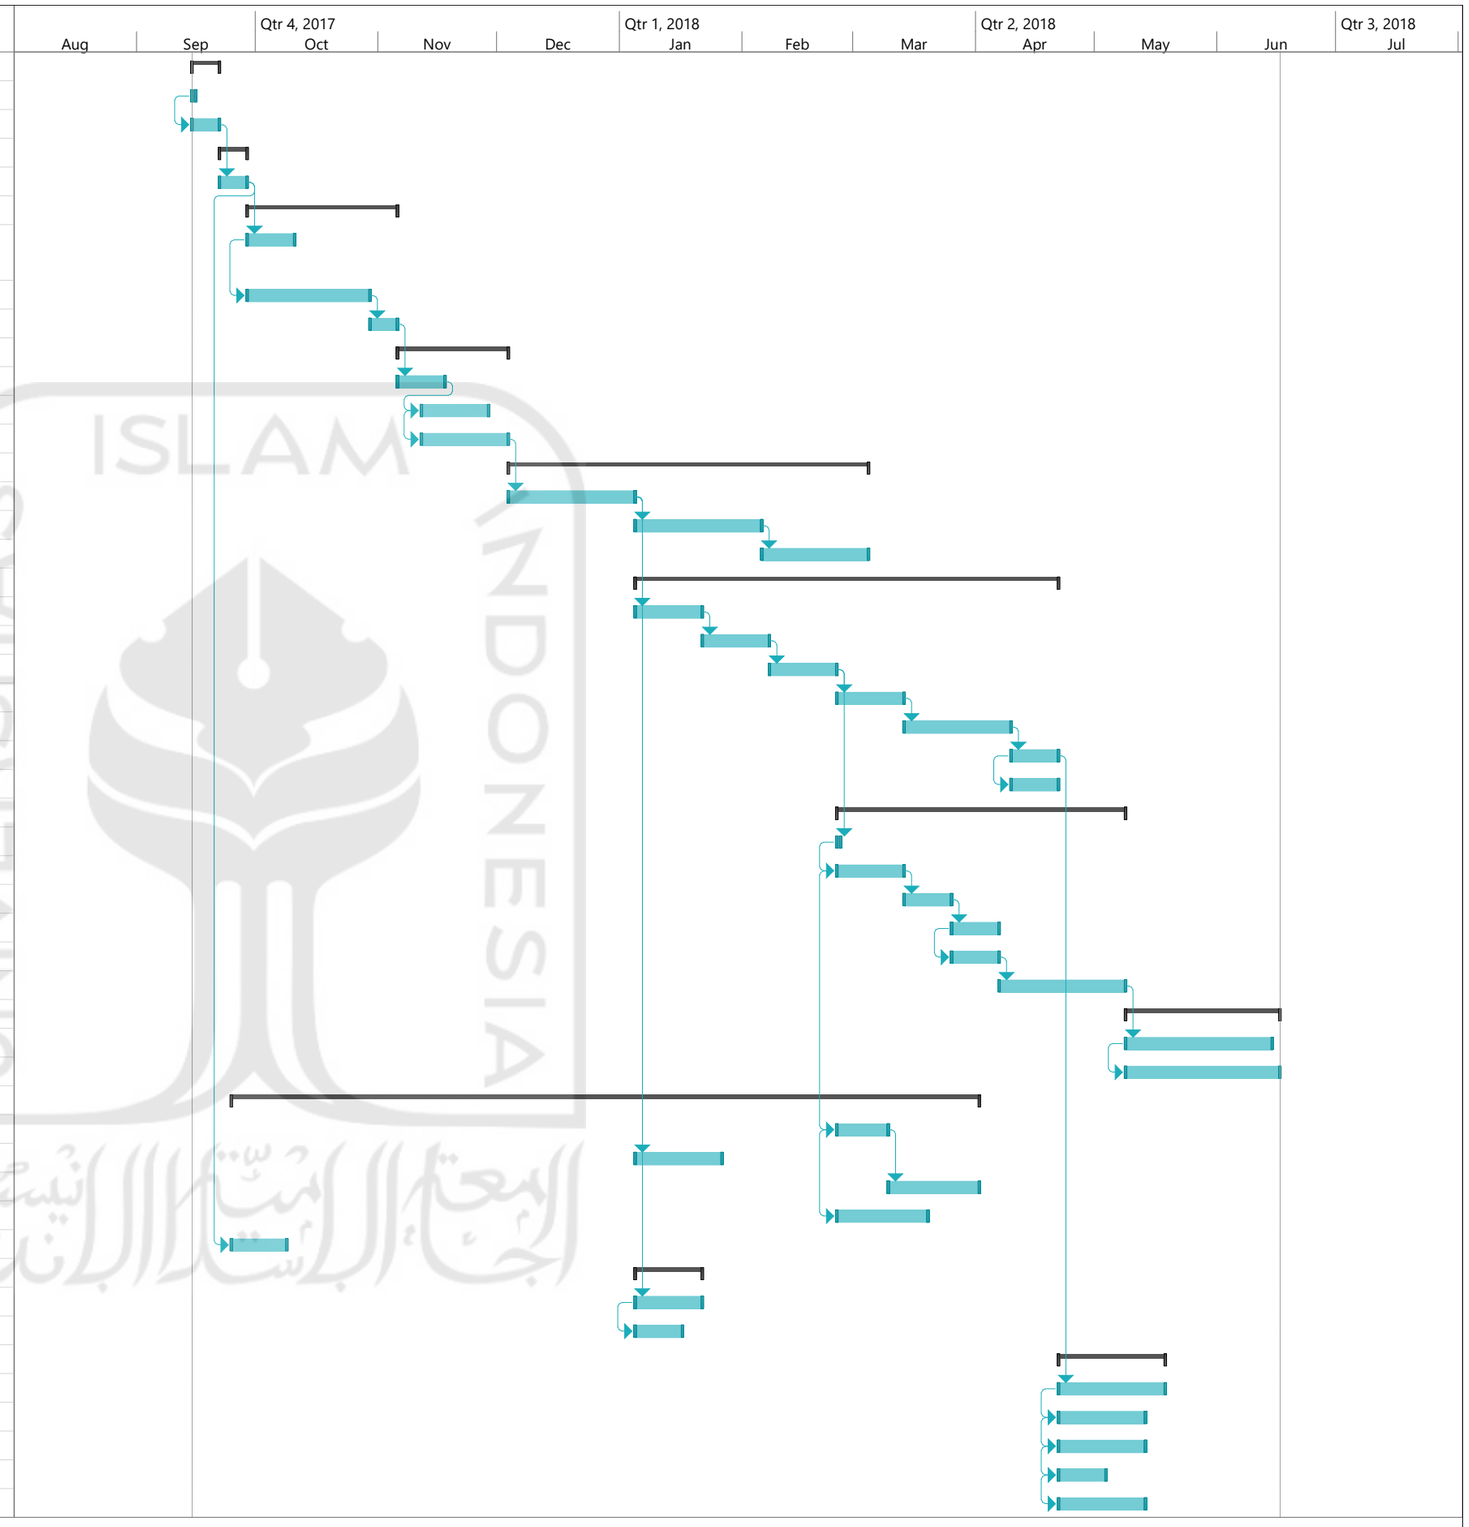ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors
1		**PEKERJAAN PERSIAPAN**	**7 days**	**15 Septembe**	**21 Septembe**	
2		Papan Nama Proyek	1 day	15 Septembe	15 Septembe	
3		Pas Bowplank	7 days	15 Septembe	21 Septembe	2SS
4		**PEKERJAAN TANAH**	**7 days**	**22 Septembe**	**28 Septembe**	
5		Galian Tanah	7 days	22 Septembe	28 Septembe	3
6		**PEKERJAAN PASANGAN**	**38 days**	**29 Septembe**	**05 Novembe**	
7		Pasangan Pondasi Batu Belah 1Pc: 4Pc	12 days	29 September	10 October	5
8		Pondasi Menara	31 days	29 Septembe	29 October	7SS
9		Urugan Tanah Kembali	7 days	30 October	05 Novembe	8
10		**PEKERJAAN BETON**	**28 days**	**06 Novembe**	**03 Decembe**	
11		Sloof	12 days	06 Novembe	17 Novembe	9
12		Kolom	17 days	12 Novembe	28 Novembe	11FS-6 days
13		Kolom Praktis	22 days	12 Novembe	03 Decembe	12SS
14		**PEKERJAAN PLASTERAN**	**91 days**	**04 Decembe**	**04 March**	
15		Pasangan Bata	32 days	04 Decembe	04 January	13
16		Plesteran Dinding	32 days	05 January	05 February	15
17		Sponengan	27 days	06 February	04 March	16
18		**PEKERJAAN ATAP DAN PLAFON**	**107 days**	**05 January**	**21 April**	
19		Ring Balk Pada Kozen	17 days	05 January	21 January	15
20		Ring Dan talang	17 days	22 January	07 February	19
21		Kuda-kuda Baja Ringan	17 days	08 February	24 February	20
22		Penutup Atap Galvalum 0,3	17 days	25 February	13 March	21
23		Plafond Gypsum	27 days	14 March	09 April	22
24		Atap Imaman	12 days	10 April	21 April	23
25		Atap KM/WC	12 days	10 April	21 April	24SS
26		**PEKERJAAN LANTAI**	**73 days**	**25 February**	**08 May**	
27		Urug Pasir Bawah Lantai	1 day	25 February	25 February	21
28		Keramik Lantai Induk	17 days	25 February	13 March	27SS
29		Keramik trap/tangga	12 days	14 March	25 March	28
30		keramik lantai KM/WC	12 days	26 March	06 April	29
31		Keramik Dinding KM/WC	12 days	26 March	06 April	30SS
32		Mainan Dinding	32 days	07 April	08 May	31
33		**PEKERJAAN CAT**	**39 days**	**09 May**	**16 June**	
34		Cat Tembok	37 days	09 May	14 June	32
35		Cat Plafond	39 days	09 May	16 June	34SS
36		**PEKERJAAN SANITASI**	**189 days**	**25 Septembe**	**01 April**	
37		Kloset Jongkok	13 days	25 February	09 March	28SS
38		Perpipaan	22 days	05 January	26 January	15
39		Kran	23 days	10 March	01 April	37
40		Floor Drain	23 days	25 February	19 March	37SS
41		Septictank	14 days	25 Septembe	08 October	5FS-4 days
42		**PEKERJAAN LISTRIK**	**17 days**	**05 January**	**21 January**	
43		Ongkos Pasang Instalasi Lampu	17 days	05 January	21 January	15
44		Onkos Pasang Instalasi Stop Kontak	12 days	05 January	16 January	43SS
45		**PEKERJAAN PINTU DAN JENDELA**	**27 days**	**22 April**	**18 May**	
46		PJ1	27 days	22 April	18 May	24
47		J1	22 days	22 April	13 May	46SS
48		J2	22 days	22 April	13 May	47SS
49		P1	12 days	22 April	03 May	48SS
50		P2	22 days	22 April	13 May	49SS
